

Highway 404 Extension

Green Lane to Ravenshoe Road

Status Update

January 12, 2011



| 1

Highway 404 Extension Green Lane to Ravenshoe Road

Construction Plan

To expedite completion, detail design and construction is being completed under four Phases:

Phase 1 - Advance Contract

- Green Lane Northbound Bridge Structure
- Completed in 2008



KEY PLAN
HIGHWAY 404 EXTENSION

Phase 2 - Advance Contract

- Mount Albert Road Overpasses
- Completed in 2009



Phase 3 - Mainline Contract 1

- From Green Lane to north of Queensville Sideroad (8 km)
- Construction started in July 2010
- Interim Completion December 2012 (complete necessary work to open to traffic)
- Final Completion – July 2013



Mainline Contract 1 (South Project) (Phase 3)

8 km: Green lane northward to Queensville Sideroad:
\$56 million contract awarded to Miller Paving.


Scope of Work Includes:

- 8 km, 4-lane divided highway
- Completion of the existing partial interchange at Green Lane and a new interchange at Queensville Sideroad
- Bridges at Doane Road and Queensville Sideroad and six large culverts for drainage and wildlife crossing
- Five stormwater management ponds
- Carpool lots at Green Lane and Queensville Sideroad. The Queensville Sideroad carpool lot includes GO Transit Facilities
- Closure of Farr Ave at Highway 404
- Provision for future HOV lanes



Phase 4 - Mainline Contract 2

- From North of Queensville Sideroad to Woodbine Ave/Ravenshoe Road (5 km)
- Schedule to tender early in 2011
- Construction start in spring 2011
- Interim Completion December 2012
(complete necessary work to open to traffic)
- Final Completion – July 2013

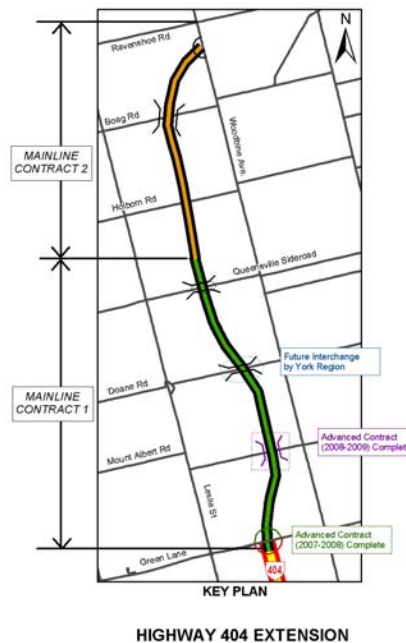

Mainline Contract 2 (North Project) (Phase 4)

5 kilometre: Queensville Sideroad to Woodbine
Avenue/Ravenshoe Road

Scope of Work Includes:

- 5 km, 4-lane divided highway
- Bridges (northbound and southbound) at Boag Road and one large culvert for drainage and wildlife crossing
- Five stormwater management ponds
- Carpool lot at Highway 404/Woodbine Ave with GO Transit Facilities
- Closure of Holborn Road at Highway 404
- Provision for future HOV lanes



Highway 404 Extension Green Lane to Ravenshoe Road

Project Status

First Mainline Contract:

- Green Lane to north of Queensville Sideroad (8 km)
- Awarded to Miller Paving for ~\$56 M in May 2010
- Construction started in July 2010. The earth grading operations are progressing slower than anticipated due to difficult soil conditions.
- Efforts continue to be made to mitigate construction delays experienced to date.
- On track to be open to traffic late 2012




Highway 404 Extension Green Lane to Ravenshoe Road

Project Status

Second Mainline Contract:

- North of Queensville Sideroad to Woodbine Ave/Ravenshoe Road (5 km)
- Detail Design is nearing completion.
- Five property owners requested a Hearing of Necessity (HN). HN was originally scheduled for June 2010, but delayed to Sept 2010 per property owners request.
- HN was held on September 21, 2010 and the inquiry officer recommended that MTO proceed with the expropriation. Property Clearance is expected in April 2011.
- Scheduled to tender early in 2011 and construction start in spring 2011.
- On track to be open to traffic late 2012

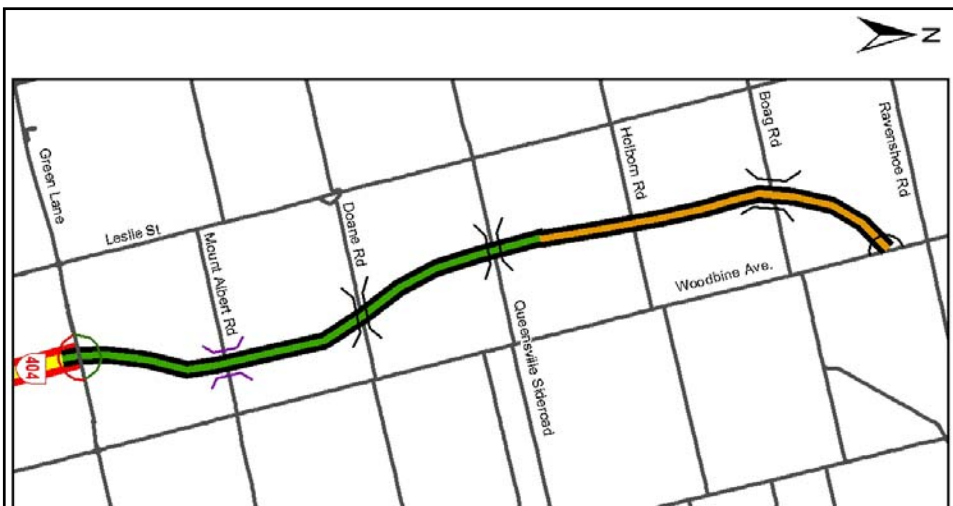

KEY PLAN

HIGHWAY 404 EXTENSION

