



Roads Capital Construction Program Update

Transportation & Works Committee

April 30, 2008

Purpose

To provide a status update of the 2008 Roads Capital Construction Program.

- ❑ Projects Recently Completed
- ❑ Projects Under Construction
- ❑ Upcoming 2008 Construction Tenders
- ❑ Upcoming 2008 Resurfacing Tenders



Ninth Line, Town of Markham

(Rose Way to Donald Cousens Parkway) - \$6.7 Million



Bathurst Street, King, Aurora & Richmond Hill

(King Road to Wellington Street) - \$10.5 Million



\$ 12.2 M

Completed Resurfacing




- Weston Road (Highway 7 to Langstaff)
- Nashville Road (Hwy. 50 to CPR)
- Yonge Street Road Rehabilitation (North of Industrial Parkway)
- Wellington Street (Dufferin to Bathurst)
- Woodbine Avenue (Old Homestead Road to Baseline Road)
- Ravenshoe Road (McCowan to Hwy. 48)
- Intersection of Major Mackenzie Drive and Keele Street
- Park Road (Ravenshoe Road to Hedge Road)
- Jane Street (Hwy. 7 to Langstaff)
- Weston Road (King-Vaughan Road to King Road)
- Jane Street (Teston Road to Highway 9)
- Ninth Line (Bloomington Road to Hillsdale)
- Intersection of Woodbine Avenue and 16th Avenue
- Kennedy Road (Stouffville Road to Bloomington)

Projects Under Construction



Teston Road, City of Vaughan

(Dufferin Street to Bathurst Street)

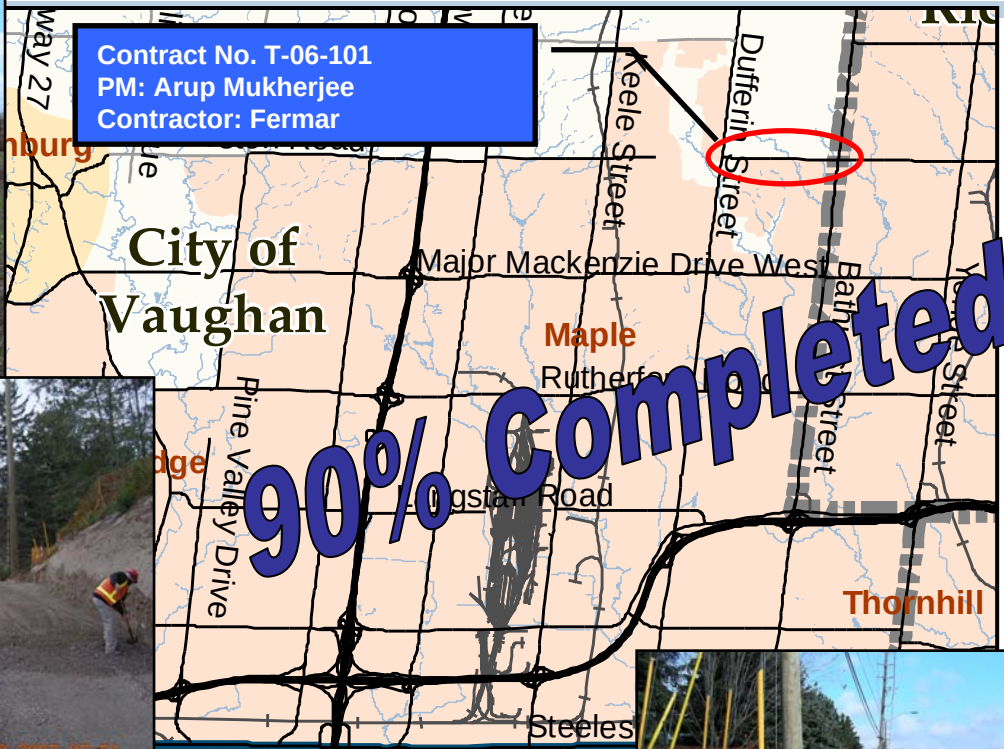


\$4.74 Million

- Start of Construction – April 2007
- Completion – June 4, 2008

Weston Road, City of Vaughan

(Major Mackenzie Drive to Teston Road)

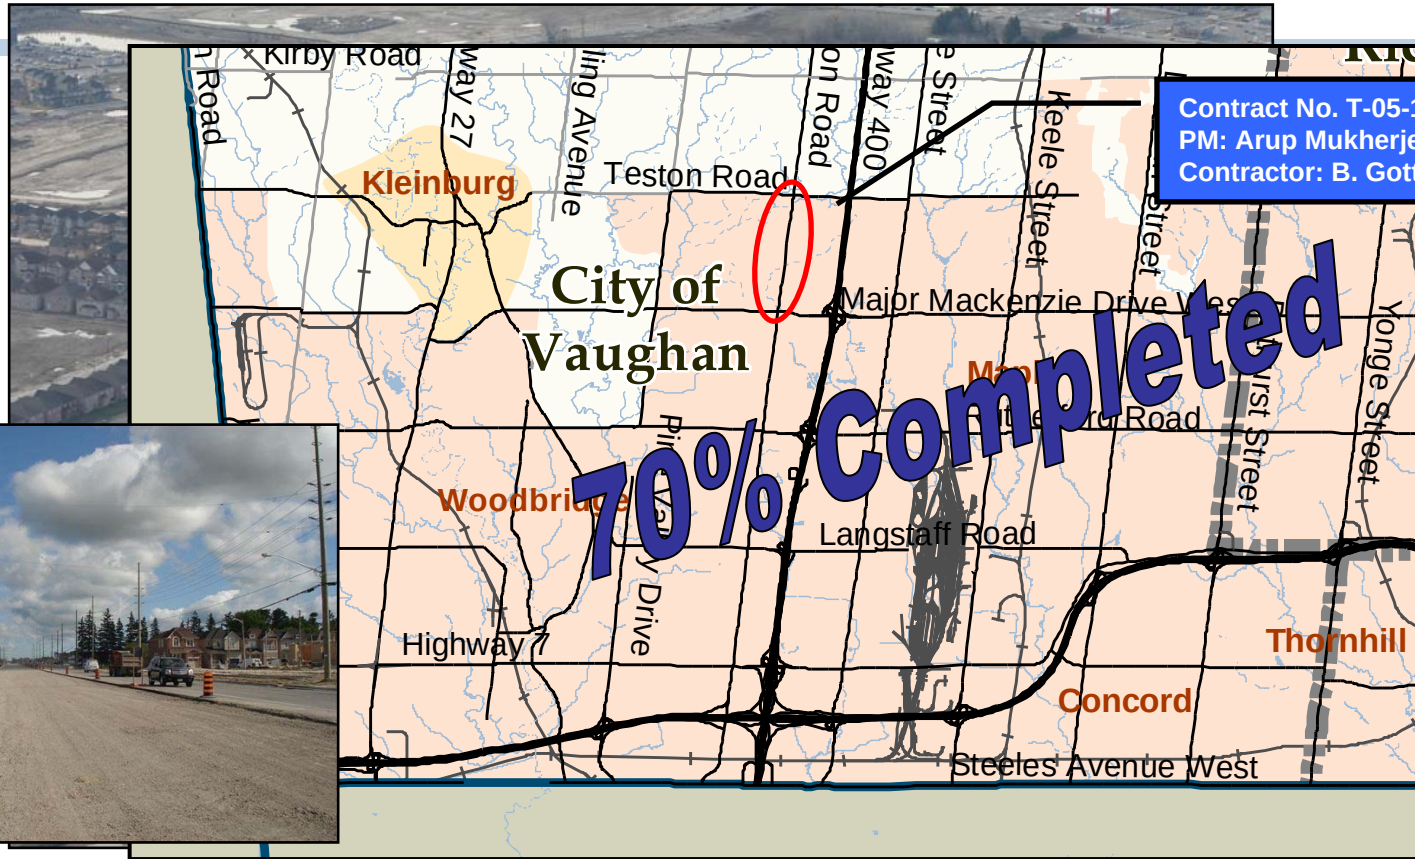


\$5.0 Million

- Start of Construction – October 2006
- Completion – November 2008

Teston Road, City of Vaughan

(Weston Road to Jane Street, including Highway 400 Interchange)

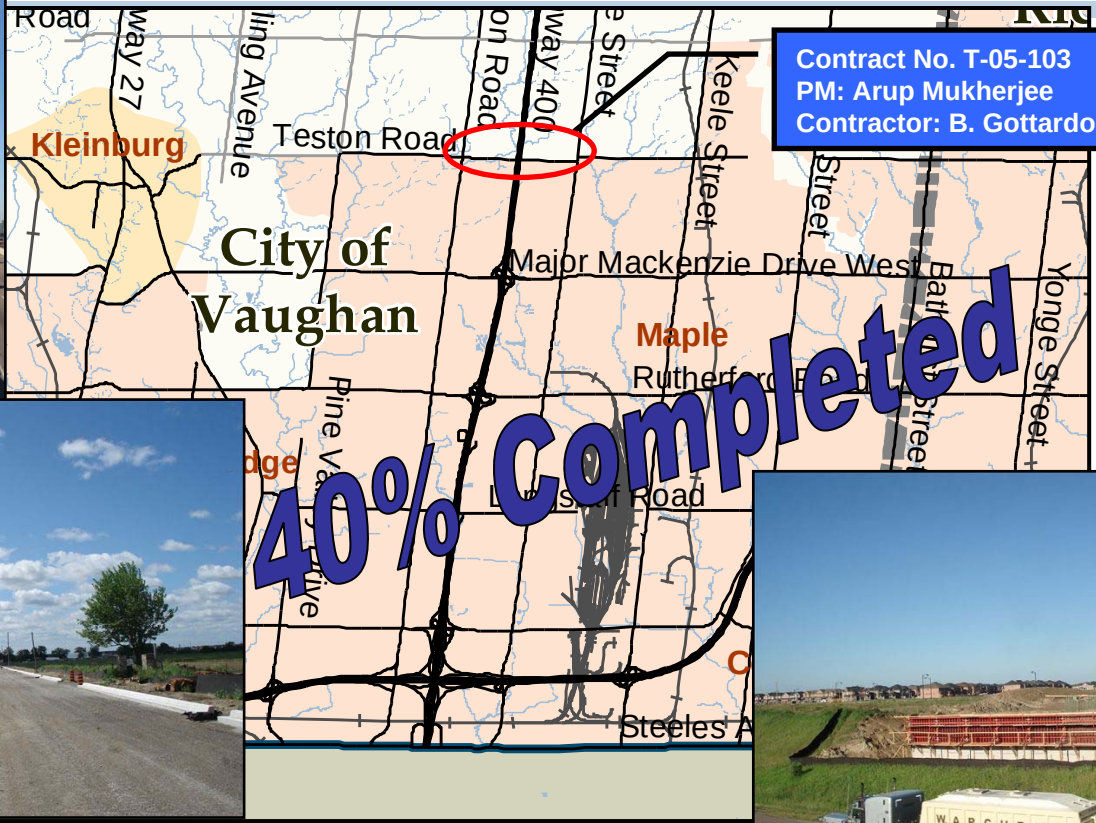

Contract No. T-05-103
PM: Arup Mukherjee
Contractor: B. Gottardo

40% Completed



\$25.5 Million

- Start of Construction – April 2007
- Re-open Road - September 2008
- Completion – Spring 2009

Teston Road, City of Vaughan

(Weston Road to Jane Street, including Highway 400 Interchange)




Teston Road, City of Vaughan

(Weston Road to Jane Street, including Highway 400 Interchange)



Highway 427 Extension, City of Vaughan

(Highway 7 to Zenway Boulevard)

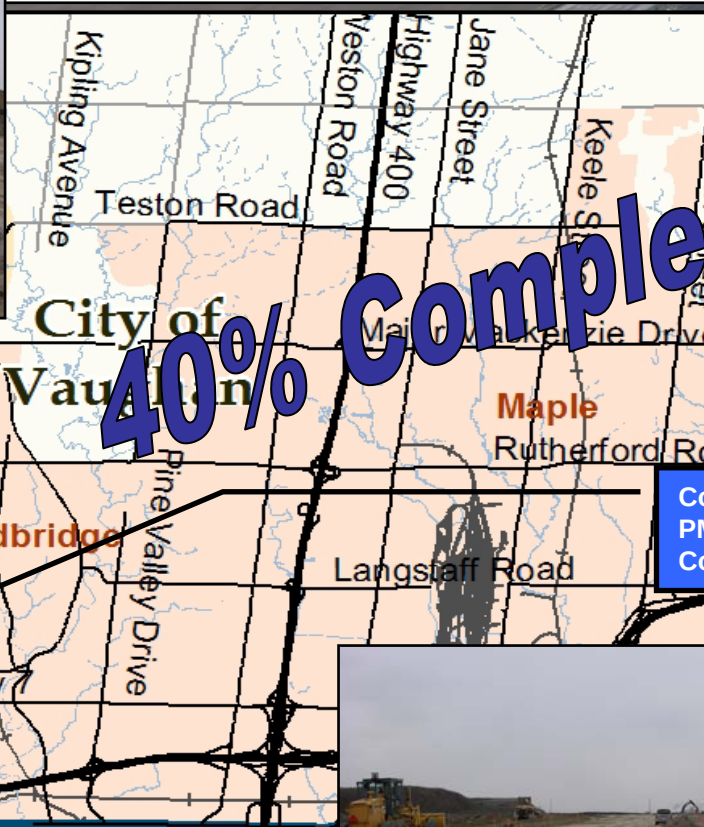


Contract No. T-07-103
PM: Nick Colarusso
Contractor: Con Drain



\$3.4 Million

- Start of Construction – October 2007
- Completion – July 15, 2008

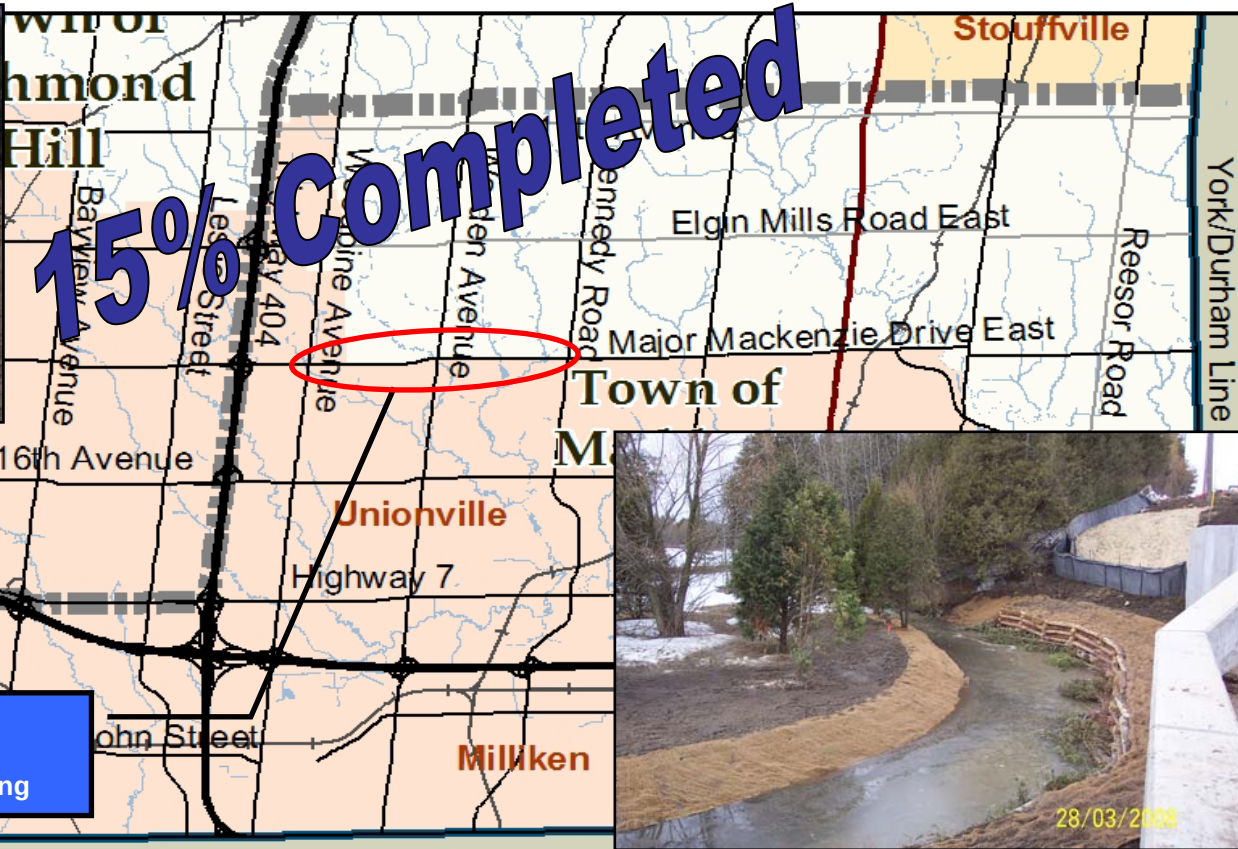

Contract No. T-07-03
PM: Peter Cholewa
Contractor: Kapp Contracting

28/03/2008

- Roads component is \$9.9 Million
- Start of Construction – September 2007
- Completion – Late 2008


Major Mackenzie Drive, Town of Markham

(Woodbine Avenue to Kennedy Road)



Ravenshoe Road, Town of Georgina

(Prout Road to Weirs' Sideroad)

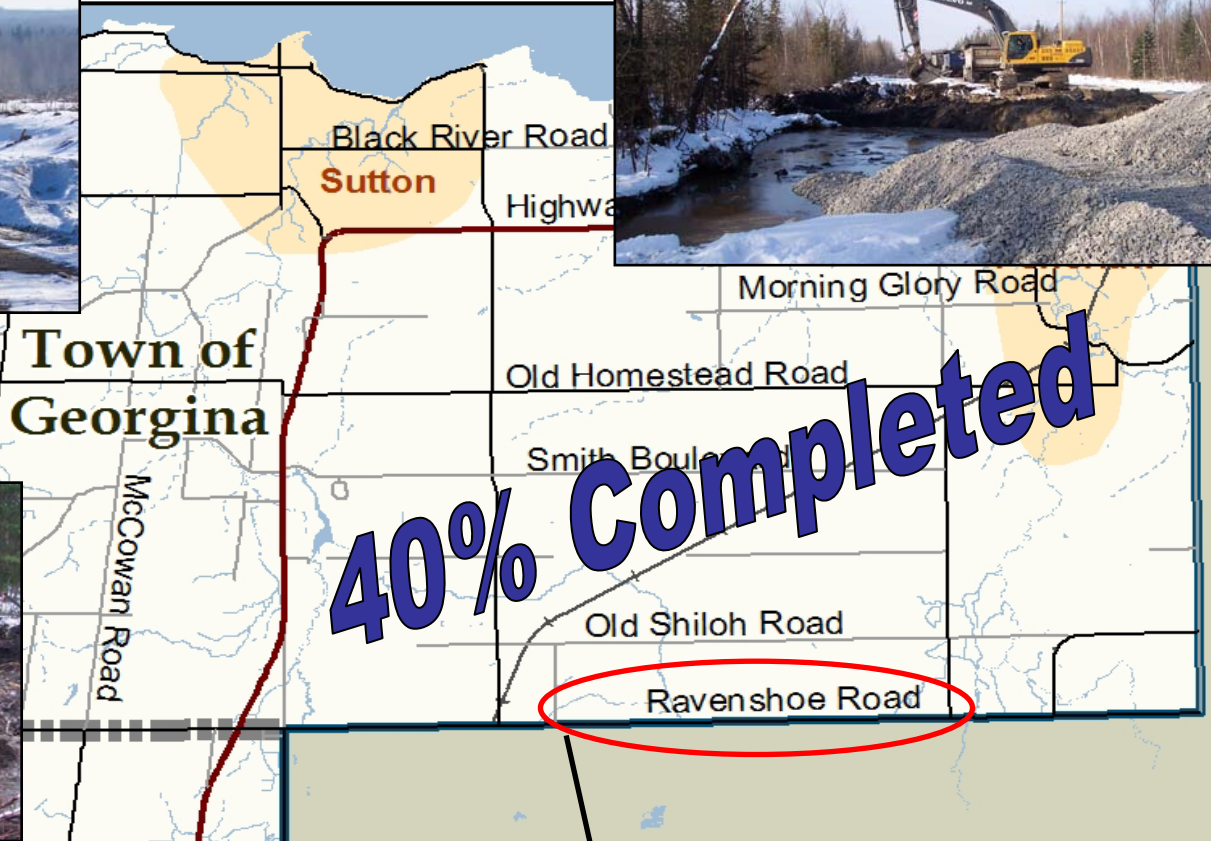


40% Completed

\$12.1 Million

- Start of Construction – January 2008
- Completion – Summer 2009

Contract No. 07-108
PM: Salim Alibhai
Contractor: K.J. Beamish

Bathurst Street, Towns of Aurora, King and Newmarket (Wellington Street to Mullock Drive)

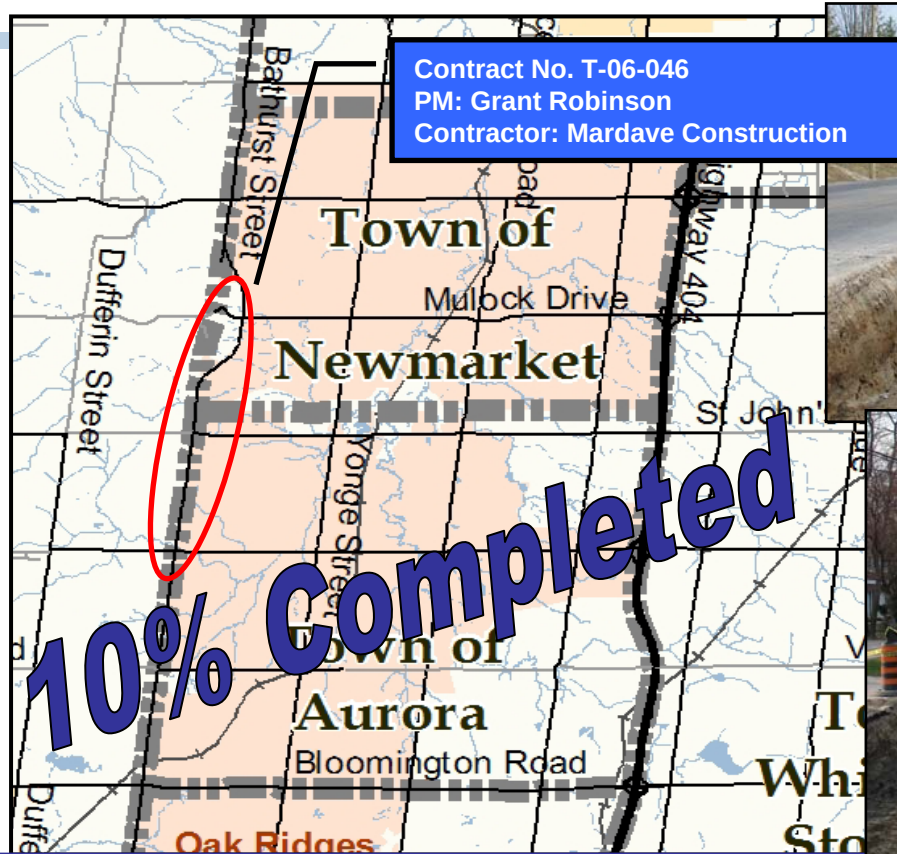

\$15.6 Million, Including Watermain

- Roads Component is \$9.7 Million
- Start of Construction – August 2007
- Completion – October 2008

Intersection Improvement, Towns of East Gwillimbury & Whitchurch-Stouffville (Warden Avenue at Davis Drive)



60% Completed



Contract No. T-07-105
PM: Arup Mukherjee
Contractor: Kapp Construction




2008.04.07 13:11

\$2.4 Million

- Start of Construction – August, 2007
- Completion – September 2008

Intersection Improvement, Town of Markham

(Kennedy Road at Birchview Lane)

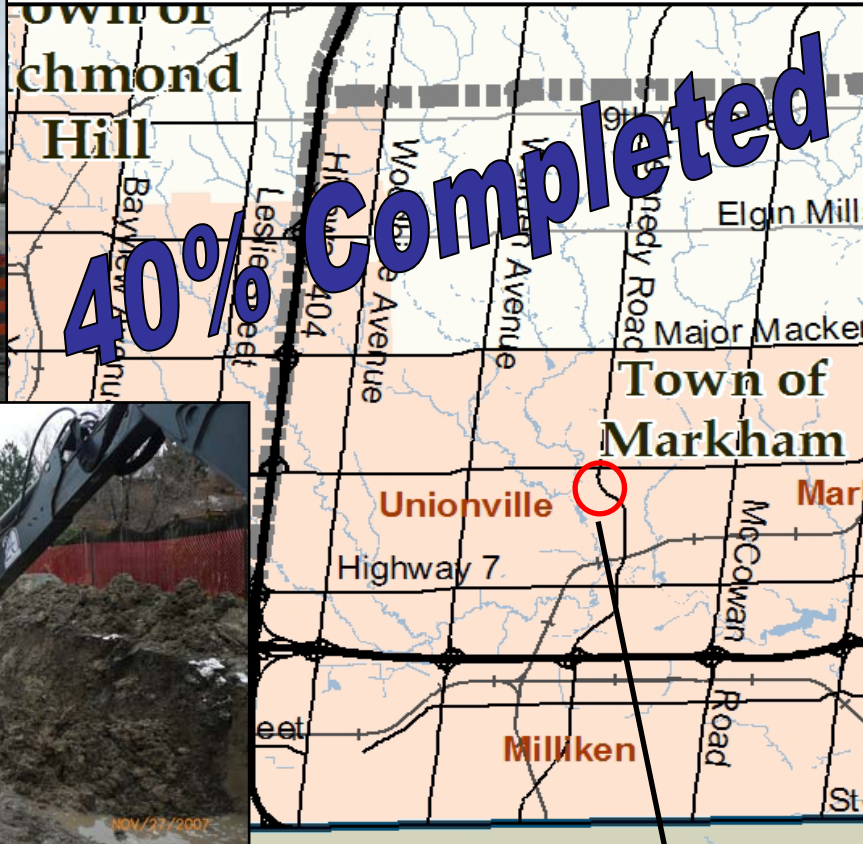


\$677 Thousand

- Start of Construction – October 2007
- Completion – July 2008

Project No. 8362
Contract No. 07-104
PM: Nick Colarusso
Contractor: Grascan

Yonge Street, Town of Aurora

(Storm Sewer Replacement)

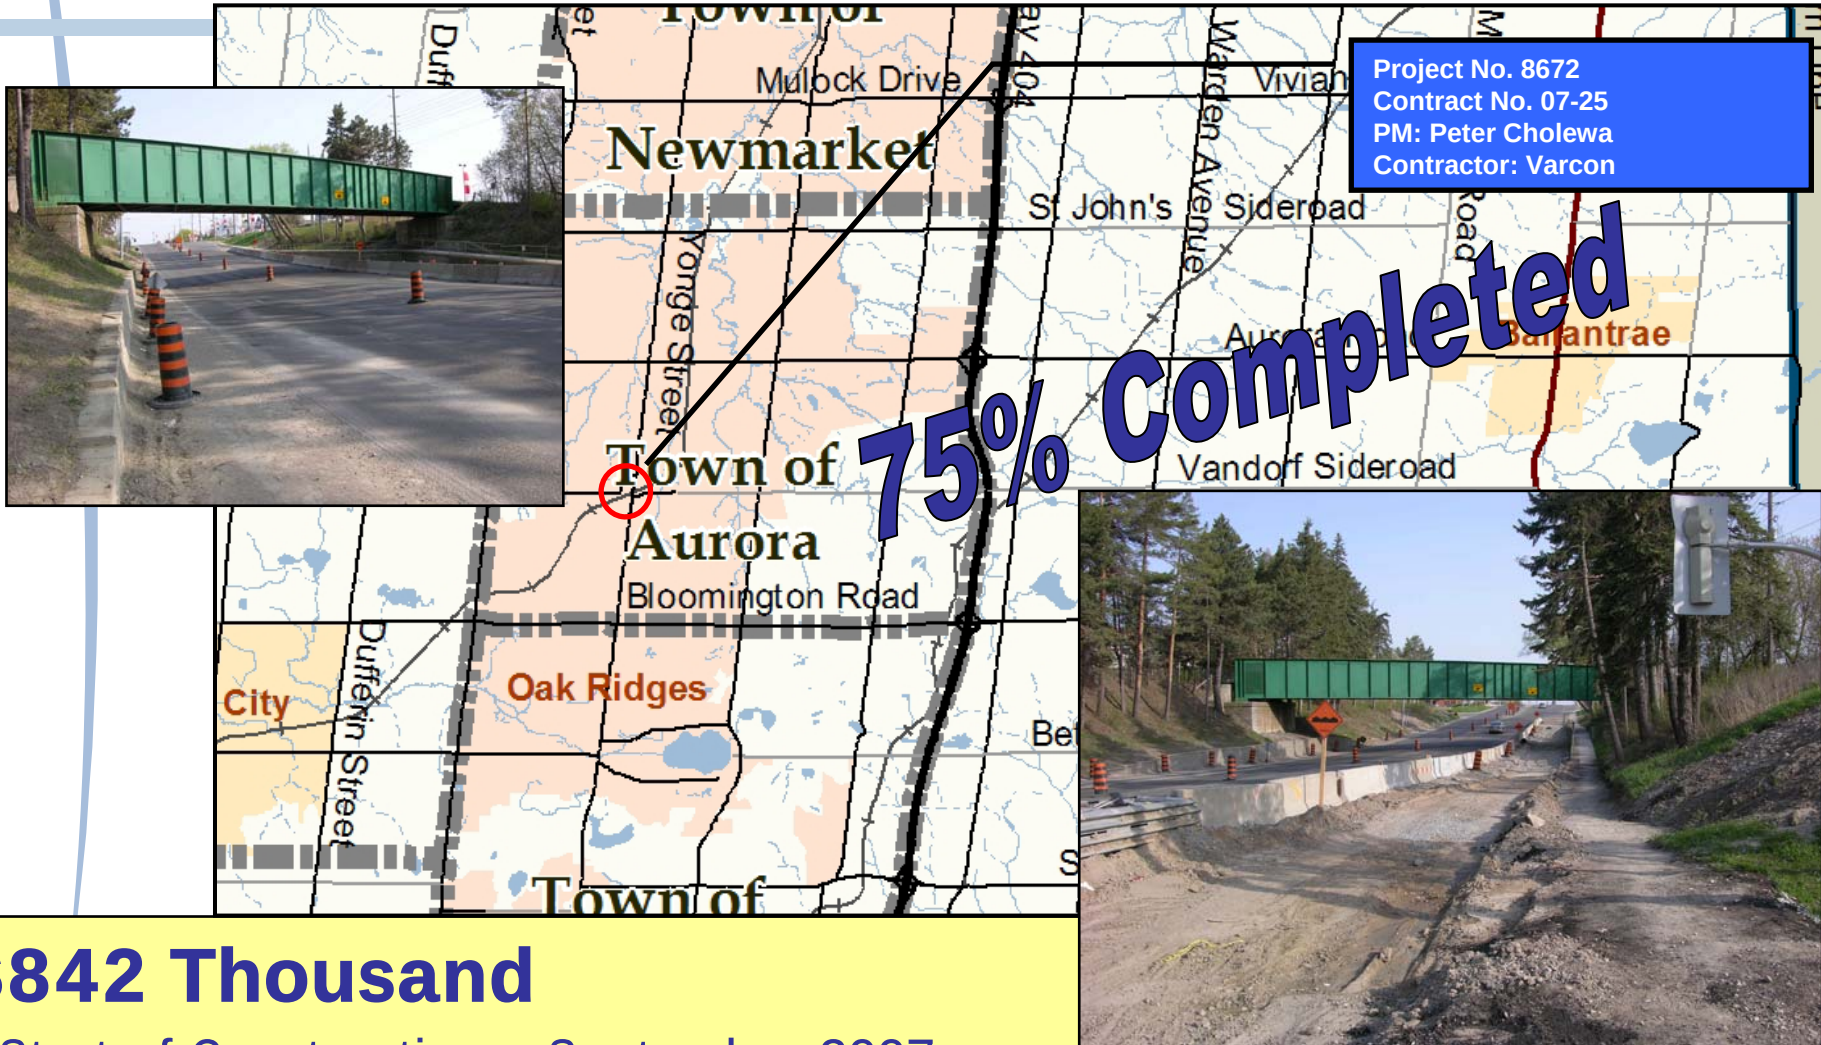

\$842 Thousand

- Start of Construction – September 2007
- Completion – May 30, 2008

Upcoming 2008 Construction Tenders



- ❑ **Dufferin Street, City of Vaughan**
(Steeles to Glen Shields Avenue)
Tender: May 2008
Completion: Late 2009
Total Project Cost: \$11.4 M
- ❑ **Ninth Line, Town of Markham**
(Highway 407 to Rose Way)
Tender: May 2008
Completion: Summer 2009
Total Project Cost: \$4.5 M
- ❑ **Bathurst Street, Town of Newmarket & Township of King**
(Mulock Drive to Highway 9)
Tender: May 2008
Completion: Spring 2009
Total Project Cost: \$6.3 M

Upcoming 2008 Construction Tenders




- ❑ **Stouffville Road, Town of Whitchurch-Stouffville**
(McCowan Road to west of Hwy. 48)
Tender: June 2008
Completion: Spring 2009
Total Project Cost: \$7.3 M
- ❑ **Stouffville Road, Town of Whitchurch-Stouffville**
(Highway 404 to Warden Avenue)
Tender: Fall 2008
Completion: Fall 2009
Total Project Cost: \$6.8 M
- ❑ **Woodbine Avenue, Town of Georgina**
(Ravenshoe Road to Morton Avenue)
Tender: Fall 2008
Completion: Fall 2009
Total Project Cost: \$17.0M

Upcoming 2008 Construction Tenders



- ❑ **Warden Avenue, Town of East Gwillimbury**
(Intersection Improvements at Mount Albert Road)
Tender: June 2008
Completion: Fall 2008
Total Project Cost: \$2.3 M

Upcoming 2008 Construction Tenders

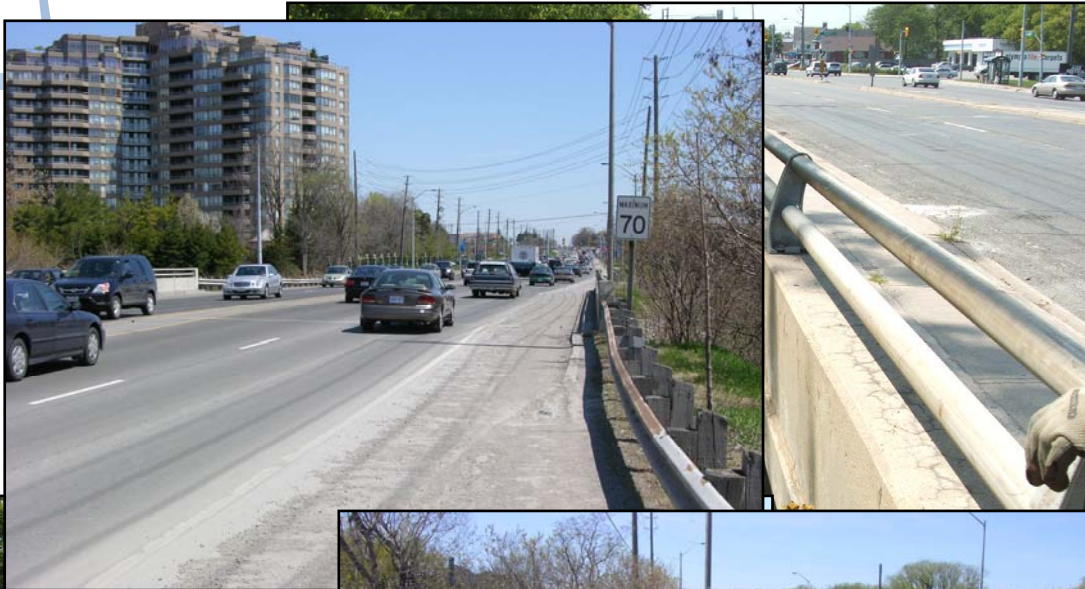


- ❑ **Highway 7, Town of Markham**
(Bridge Rehabilitation west of Kennedy Road)
Tender: May 2008
Completion: Fall 2008
Total Project Cost: \$0.8M



- ❑ **Highway 7, Town of Markham**
(Bridge Rehabilitation west of McCowan Road)
Tender: May 2008
Completion: Fall 2008
Total Project Cost: \$1.0 M

\$ 18.3M

Upcoming Resurfacing Projects

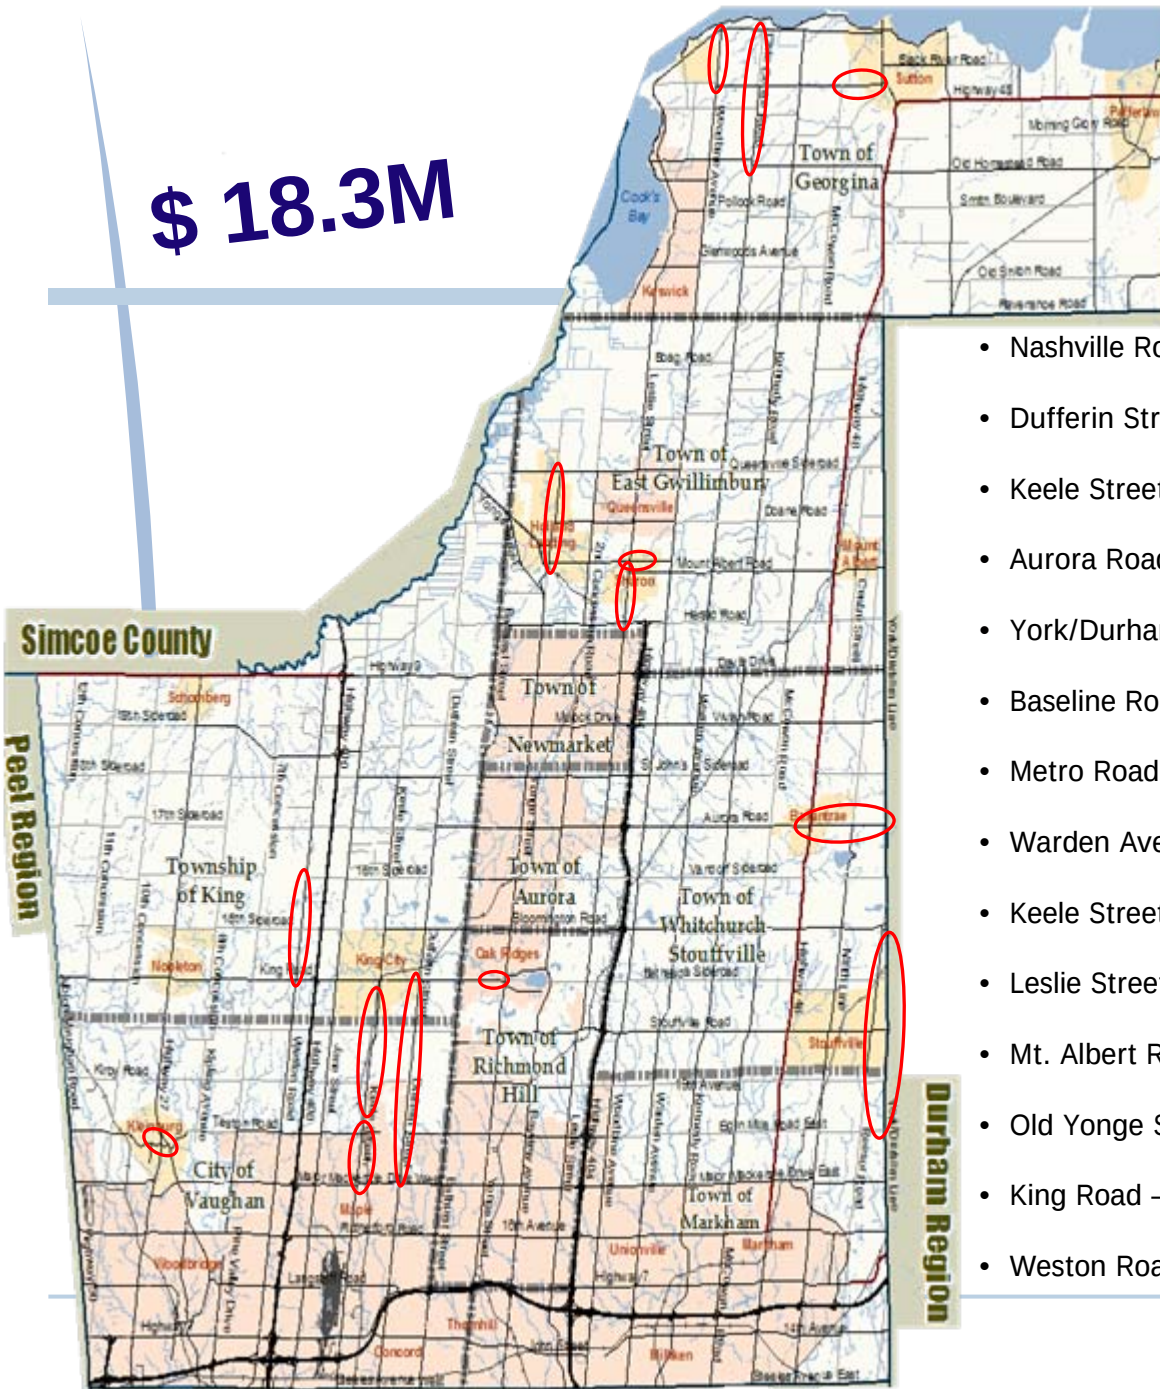

- Nashville Road (E of Huntington Road to Hwy. 27)
- Dufferin Street (Major Mackenzie Dr. to King Road)
- Keele Street Teston Road to Station Road)
- Aurora Road – Hwy. 48 to York/Durham Line
- York/Durham Line – Elgin Mills Road to 10th Line
- Baseline Road – McCowan Rd. to Dalton Rd.
- Metro Road – Kennedy Road to Salvation Army Road
- Warden Avenue – Old Homestead to Baseline Road
- Keele Street – Major Mackenzie Drive to Teston Road
- Leslie Street – Green Lane to Mount Albert Road
- Mt. Albert Road – Leslie St. to Colonel Wayling Blvd.
- Old Yonge Street – Mt. Albert to Queensville Sdrd.
- King Road – Yonge Street to Bond Crescent
- Weston Road – King Road to 16th Sideroad

Summary

- ❑ **2 Projects Already Completed - \$17.2M**
- ❑ **10 Projects Under Construction - \$74.3M**
 - ❑ **(\$49.7M in 2008 Dollars)**
- ❑ **11 Projects to be Tendered by Year End - \$78.5M**
- ❑ **Approximately \$27.9 M (2009 Dollars) will be committed in these tenders**

